



DOC ID: SL-POP-ERP-SUMMARY-001

Consolidated Release: October 2026 • Ver 1.0 Final

MASTER EXECUTIVE PORTFOLIO & FINANCIAL ROADMAP

## Popular Auto Spare ERP — Complete 9-Module Master Milestone & Budget Summary

Executive consolidated milestone breakdown, multi-module timeline mapping, engineering resource matrix, and grand commercial investment schedule for Popular Auto Spare & A/C Parts Co. W.L.L. Prepared by SaNDS Lab Middle East W.L.L in strategic alignment with UniGlobal Consultancy.

TOTAL MODULES

**9 Modules**

End-to-End Automotive ERP

TOTAL INVESTMENT

**BD 34,090.910**

Fixed Baseline in Bahraini Dinars

CUMULATIVE EFFORT

**88 Weeks**

17.6 Engineering Months

DEDICATED TEAM

**5 Specialists**

100% Dedicated Full-Time

VERIFICATION TRANCHES

**35 Gates**

Zero-Risk Milestones



**9 / 9**

Modules Documented

Complete functional & technical specs



**BD 1,363.636**

Monthly Team Burn-Rate

Fixed transparent rate card



**100% Multi-Branch**

Enterprise Coverage

Warehouses, POS counters, mobile floor



**15-Day UAT**

Acceptance Grace SLA

Rigorous milestone verification



### Total Fixed Project Investment (All 9 Modules)

Unified contract value covering the complete design, engineering, multi-branch testing, data migration, hardware integrations, training, and production deployment across all 9 modules for Popular Auto Spare & A/C Parts Co. W.L.L.

**BD 34,090.910**

THIRTY-FOUR THOUSAND NINETY BAHRAINI DINARS & 910 FILS


 Visual Milestone & Budget Analytics

Visualizing budget distribution and engineering effort allocation across all 9 modules

INTERACTIVE VISUAL INSIGHTS

 Budget Distribution by Module (BHD)


Total: BD 34,090.910

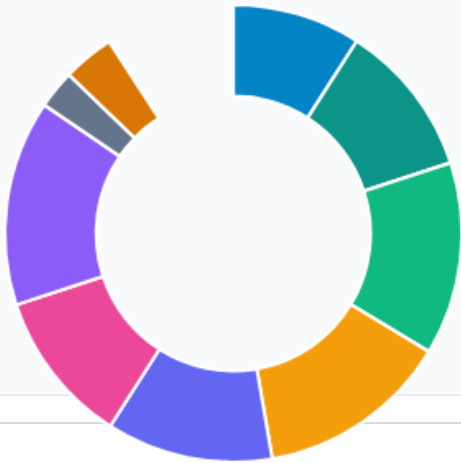

- M1: PCode & Item Master
- M2: Vendor & Purchase
- M3: Store Verification
- M4: Sales & POS Billing
- M5: Accounts & VAT
- M6: Enterprise Admin
- M7: HRM & Payroll
- M8: Hardware & Servers
- M9: Executive BI Dashboai

 Engineering Timeline by Module (Weeks)

Total: 88 Working Weeks

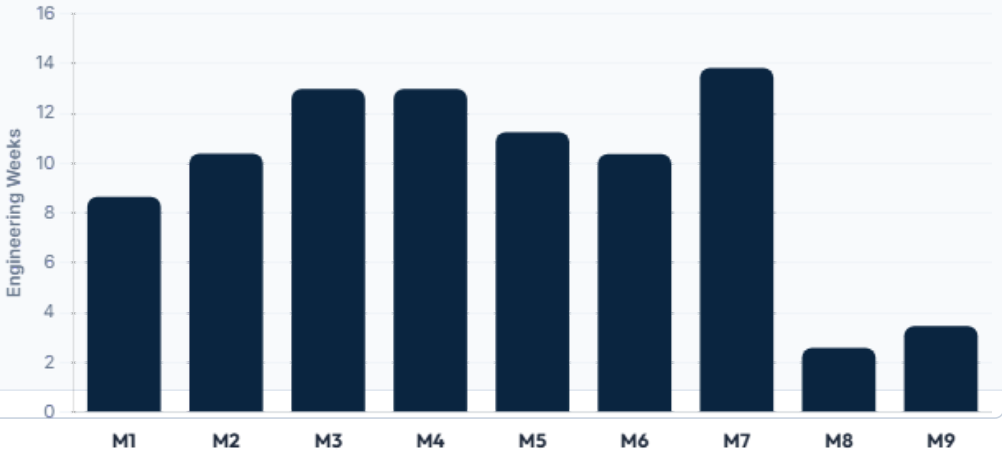

 Master 9-Module Budgeting & Milestone Matrix (BHD)

At-a-glance comparative overview of all 9 modules, timelines, effort, deliverables, and total fees in Bahraini Dinars

ALL AMOUNTS IN BAHRAINI DINARS (BHD)

| #                                                       | Module Scope & Implementation Domain                                                                                                           | Timeline | Effort   | Milestone Gates | Total Cost (BHD) | Weekly Burn | Share (%) | Action     |
|---------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------|----------|----------|-----------------|------------------|-------------|-----------|------------|
| 1                                                       | <div>SL-P0P-ERP-MS-001</div> <div>BA Ref: DOC-001 v1.0</div> <div>PCode Generation, Cataloguing &amp; Item Master Engine</div>                 | 10 Weeks | 2.50 Mo  | 4 Gates (25%)   | BD 3,409.091     | BD 340.909  | 10.00%    |            |
| 2                                                       | <div>SL-P0P-ERP-MS-002</div> <div>BA Ref: DOC-002 v1.0</div> <div>Vendor &amp; Purchase Management, Supplier Portal &amp; 3-Way Match</div>    | 12 Weeks | 3.00 Mo  | 4 Gates (25%)   | BD 4,090.909     | BD 340.909  | 12.00%    |            |
| 3                                                       | <div>SL-P0P-ERP-MS-003</div> <div>BA Ref: DOC-003 v1.0</div> <div>Store Verification, Multi-Warehouse Stock &amp; Location Matrix</div>        | 15 Weeks | 3.75 Mo  | 4 Gates (25%)   | BD 5,113.636     | BD 340.909  | 15.00%    |            |
| 4                                                       | <div>SL-P0P-ERP-MS-004</div> <div>BA Ref: DOC-004 v1.0</div> <div>Sales Process, Mobile POS, Multi-Branch Billing &amp; Return Control</div>   | 15 Weeks | 3.75 Mo  | 4 Gates (25%)   | BD 5,113.636     | BD 340.909  | 15.00%    |            |
| 5                                                       | <div>SL-P0P-ERP-MS-005</div> <div>BA Ref: DOC-005 v1.0</div> <div>Accounting &amp; Financial Management, General Ledger, AP/AR &amp; VAT</div> | 13 Weeks | 3.25 Mo  | 4 Gates (25%)   | BD 4,431.818     | BD 340.909  | 13.00%    |            |
| 6                                                       | <div>SL-P0P-ERP-MS-006</div> <div>BA Ref: DOC-006 v1.0</div> <div>Enterprise Administration, Facility, Fixed Assets, Fleet &amp; Vault</div>   | 12 Weeks | 3.00 Mo  | 4 Gates (25%)   | BD 4,090.909     | BD 340.909  | 12.00%    |            |
| 7                                                       | <div>SL-P0P-ERP-MS-007</div> <div>BA Ref: DOC-007 v1.0</div> <div>Human Resource Management, Biometrics, Leave, Payroll &amp; Gratuity</div>   | 16 Weeks | 4.00 Mo  | 4 Gates (25%)   | BD 5,454.548     | BD 340.909  | 16.00%    |            |
| 8                                                       | <div>SL-P0P-ERP-MS-008</div> <div>BA Ref: ARCH-001 v1.0</div> <div>Hardware Setup, Handheld QR Devices, ESC/POS &amp; Cloud Cluster</div>      | 3 Weeks  | 0.75 Mo  | 3 Gates (33%)   | BD 1,022.727     | BD 340.909  | 3.00%     |            |
| 9                                                       | <div>SL-P0P-ERP-MS-009</div> <div>BA Ref: DOC-009 v1.0</div> <div>Executive Management Dashboard, 8-Module BI &amp; Mobile Cockpit</div>       | 4 Weeks  | 1.00 Mo  | 4 Gates (25%)   | BD 1,363.636     | BD 340.909  | 4.00%     |            |
| GRAND TOTAL: COMPLETE 9-MODULE AUTOMOTIVE ERP PORTFOLIO |                                                                                                                                                | 88 Weeks | 17.60 Mo | 35 Gates        | BD 34,090.910    | BD 387.397  | 100.00%   | Full Suite |



## 9-Module Architectural Scope & Deliverable Pillars

Key functional scope, core modules, and business impact for Popular Auto Spare Co.

FUNCTIONAL PORTFOLIO

### MODULE 1

BD 3,409.091

#### PCode Generation & Universal Item Master

Automated smart PCode generation algorithms, multi-brand hierarchy (Car Make/Model/Year), 1-to-Many OEM cross-reference matrix, 50,000+ SKU legacy data cleansing, and sub-100ms multi-parameter fuzzy search.

🕒 10 Weeks (2.5 Mo)

### MODULE 2

BD 4,090.909

#### Vendor & Purchase Management with 3-Way Match

Multi-country vendor master, tokenized supplier RFQ portal, MOQ reorder buffering, CTO purchase approvals, automated PO splits by brand, Goods Receipt Note (GRN) with landed cost, and 3-way invoice matching.

🕒 12 Weeks (3.0 Mo)

### MODULE 3

BD 5,113.636

#### Store Verification & Multi-Warehouse Stock Control

5-tier warehouse spatial layout (Zone/Aisle/Rack/Shelf/Bin), handheld Android scanner engine, blind 60/40 cycle counts, inter-branch stock transfers (GIT) with driver signatures, and FIFO inventory valuation.

🕒 15 Weeks (3.75 Mo)

### MODULE 4

BD 5,113.636

#### Sales Process, Mobile POS & Branch Cash Control

High-speed counter POS, mobile Android handheld floor sales, dynamic QR cart handoff, credit customer credit-risk limits, verified invoice returns with condition grading, and End-of-Day cash drawer closing locks.

🕒 15 Weeks (3.75 Mo)

### MODULE 5

BD 4,431.818

#### Accounting, General Ledger, AP/AR & VAT Compliance

5-group Chart of Accounts (COA), real-time double-entry GL, automated AP/AR subledgers, multi-currency treasury, automated Bank Reconciliation (BRS), PDC management, and Bahrain NBR 10% VAT return filings.

🕒 13 Weeks (3.25 Mo)

### MODULE 6

BD 4,090.909

#### Enterprise Administration, Fixed Assets & Fleet

Centralized branch facility ticketing, fixed asset QR tagging with automated straight-line depreciation, company vehicle fleet logs with Total Cost of Ownership (TCO), and legal document expiry alerts (CR, Leases).

🕒 12 Weeks (3.0 Mo)

### MODULE 7

BD 5,454.548

#### HR Management, Biometrics, Payroll & Gratuity

Employee 360 master, physical biometric clock-in & geofenced mobile attendance, Bahrain Labour Law leave rules, automated monthly payroll engine, SIO/LMRA/WPS bank export, and End-of-Service Benefit (EOSB) settlements.

🕒 16 Weeks (4.0 Mo)

### MODULE 8

BD 1,022.727

#### Hardware Setup, Scanners, Printers & Cloud Cluster

3-tier cloud server architecture (Dev / Staging / Prod), RabbitMQ asynchronous background queue, Android PDA scanner listeners, ESC/POS thermal receipt & barcode label printers, and biometric sync daemons.

🕒 3 Weeks (0.75 Mo)

### MODULE 9

BD 1,363.636

#### Executive Management Dashboard & BI Cockpit

OLAP data warehouse aggregation engine, real-time KPI metrics across all 8 modules, automated anomaly detection, daily 7:00 AM WhatsApp/Email executive digest, and secure C-Suite mobile executive reporting.

🕒 4 Weeks (1.0 Mo)

## Complete 35 Milestone Tranches Detailed Breakdown (BHD)

Specific milestone gates, percentages, exact BHD allocations, and payment triggers for each phase

35 MILESTONE TRANCHES

### MOD 1 Module 1: PCode Generation & Item Master Engine (10 Weeks)

BD 3,409.091

#### MILESTONE 1.1 (25%)

BD 852.273

PCode DB Schema, Data Cleansing Engine & Base Generation Algorithm.

📅 Weeks 1-3

#### MILESTONE 1.2 (25%)

BD 852.273

Brand / Model / Spec Dynamic Hierarchy & Automated PCode Generator Engine.

📅 Weeks 4-5

#### MILESTONE 1.3 (25%)

BD 852.273

Universal Cross-Reference / Interchange Matrix & Barcode Tagging Engine.

📅 Weeks 6-8

#### MILESTONE 1.4 (25%)

BD 852.273

Real-Time Search, Legacy Migration (50,000+ SKUs) & Multi-Branch Final UAT.

📅 Weeks 9-10

### MOD 2 Module 2: Vendor & Purchase Management (12 Weeks)

BD 4,090.909

#### MILESTONE 2.1 (25%)

BD 1,022.727

Supplier Master, Tokenized Vendor Portal & Automated RFQ Engine.

📅 Weeks 1-3

#### MILESTONE 2.2 (25%)

BD 1,022.727

Multi-Vendor Quotation Evaluation Matrix & Automated PO Split Engine.

📅 Weeks 4-6

#### MILESTONE 2.3 (25%)

BD 1,022.727

Goods Receipt Note (GRN), Multi-Currency Landed Cost & QC Inspection.

📅 Weeks 7-9

#### MILESTONE 2.4 (25%)

BD 1,022.727

3-Way Invoice Matching, Vendor SLA Scorecards & Multi-Branch Sign-Off.

📅 Weeks 10-12

### MOD 3 Module 3: Store Verification & Stock Control (15 Weeks)

BD 5,113.636

#### MILESTONE 3.1 (25%)

BD 1,278.409

Warehouse Spatial Hierarchy (5 Tiers), Bin Matrix & Inward PVN Setup.

📅 Weeks 1-4

#### MILESTONE 3.2 (25%)

BD 1,278.409

Handheld Scanner Engine, Blind 60/40 Cycle Counts & Variance Alerts.

📅 Weeks 5-8

#### MILESTONE 3.3 (25%)

BD 1,278.409

Inter-Branch Stock Transfers (GIT), Multi-Tier Discrepancy & FIFO Valuation.

📅 Weeks 9-12

#### MILESTONE 3.4 (25%)

BD 1,278.409

Min/Max Safety Stock Auto-Replenishment, Aging & Final Warehouse Sign-Off.

📅 Weeks 13-15

### MOD 4 Module 4: Sales Process, POS & Branch Financial Control (15 Weeks)

BD 5,113.636

#### MILESTONE 4.1 (25%)

BD 1,278.409

Multi-Branch POS Architecture, Offline Sync & Cash Drawer Session Control.

📅 Weeks 1-4

#### MILESTONE 4.2 (25%)

BD 1,278.409

Counter & Mobile Handheld POS Billing, Multi-Price Matrix & Barcodes.

📅 Weeks 5-8

#### MILESTONE 4.3 (25%)

BD 1,278.409

Credit Customer Governance, Credit Limit Locks, Delivery Notes & B2B Invoices.

📅 Weeks 9-12

#### MILESTONE 4.4 (25%)

BD 1,278.409

Verified Sales Returns, End-of-Day Branch Reconciliation & Audit UAT.

📅 Weeks 13-15

### MOD 5 Module 5: Accounting & Financial Management (13 Weeks)

BD 4,431.818

#### MILESTONE 5.1 (25%)

BD 1,107.955

Dynamic Chart of Accounts (COA), Cost Centers & Auto Journal Engine.

#### MILESTONE 5.2 (25%)

BD 1,107.955

AP / AR Subledgers, Aging Analysis, Statements & Credit Lock Rules.

#### MILESTONE 5.3 (25%)

BD 1,107.955

Multi-Currency Treasury, Automated Bank Reconciliation & Cashflow Engine.

#### MILESTONE 5.4 (25%)

BD 1,107.955

Bahrain NBR 10% VAT Return Generator, Balance Sheet, P&L & Final Sign-Off.

📅 Weeks 1–3

📅 Weeks 4–6

📅 Weeks 7–10

📅 Weeks 11–13

**MOD 6**   **Module 6: Enterprise Administration & Fixed Assets (12 Weeks)**

**BD 4,090.909**   ▾

**MILESTONE 6.1 (25%)**

**BD 1,022.727**

Facility Management, Maintenance Ticketing, Utility Logs & Lease Alerts.

📅 Weeks 1–3

**MILESTONE 6.2 (25%)**

**BD 1,022.727**

Fixed Asset Master, QR Tagging, Custodian Tracking & Depreciation Engine.

📅 Weeks 4–6

**MILESTONE 6.3 (25%)**

**BD 1,022.727**

Fleet Logistics, Vehicle Bookings, Fuel Reconciliation & TCO Analytics.

📅 Weeks 7–9

**MILESTONE 6.4 (25%)**

**BD 1,022.727**

Staff Locker Control, Secure Digital Document Vault & CR Renewal Alerts.

📅 Weeks 10–12

**MOD 7**   **Module 7: Human Resource Management & Payroll (16 Weeks)**

**BD 5,454.548**   ▾

**MILESTONE 7.1 (25%)**

**BD 1,363.637**

Org Structure, Employee Master, Document Vault & Digital Onboarding.

📅 Weeks 1–4

**MILESTONE 7.2 (25%)**

**BD 1,363.637**

Biometric Attendance, Shift Rosters & Bahrain Labour Law Leave System.

📅 Weeks 5–8

**MILESTONE 7.3 (25%)**

**BD 1,363.637**

Automated Payroll, SIO/LMRA Compliance, WPS/CBB Export & Loan Advances.

📅 Weeks 9–12

**MILESTONE 7.4 (25%)**

**BD 1,363.637**

Performance KPIs, ESS Self-Service Portal, EOSB Gratuity & Production Go-Live.

📅 Weeks 13–16

**MOD 8**   **Module 8: Hardware Integration & Cloud Cluster (3 Weeks)**

**BD 1,022.727**   ▾

**MILESTONE 8.1 (33.33%)**

**BD 340.909**

3-Tier Server Environment (Dev/Stage/Prod), RabbitMQ & Backup Automation.

📅 Week 1

**MILESTONE 8.2 (33.33%)**

**BD 340.909**

Handheld Android QR Scanners, ESC/POS Printers & Biometric Clocks.

📅 Week 2

**MILESTONE 8.3 (33.34%)**

**BD 340.909**

Offline Auto-Sync Engine, Multi-Branch Stress Testing & Go-Live.

📅 Week 3

**MOD 9**   **Module 9: Executive Management Dashboard & BI Cockpit (4 Weeks)**

**BD 1,363.636**   ▾

**MILESTONE 9.1 (25%)**

**BD 340.909**

Data Warehouse OLAP Schema, Non-Blocking ETL Pipelines & KPI Models.

📅 Week 1

**MILESTONE 9.2 (25%)**

**BD 340.909**

Commercial, Stock Velocity, Warehouse Verification & Vendor SLA Cockpit.

📅 Week 2

**MILESTONE 9.3 (25%)**

**BD 340.909**

Financial Liquidity, VAT, HR Payroll, Fixed Assets & Infra Health Analytics.

📅 Week 3

**MILESTONE 9.4 (25%)**

**BD 340.909**

Management Filtering, 7:00 AM WhatsApp/Email Digest & Final Sign-Off.

📅 Week 4

 **Dedicated Engineering Team & Transparent Rate Matrix**

Full-time dedicated 5-person engineering team rate card in Bahraini Dinars (BHD)

TEAM MONTHLY RATE: BD 1,363.636

All modules are estimated strictly using the agreed dedicated team rate matrix in Bahraini Dinars (BHD). Total dedicated team capacity: 160 hours / month per engineer.

Project Manager & Enterprise Solutions Architect

BD 545.455

BD 136.364 / Wk • BD 3.409 / Hr

100% Dedicated

Back-End Lead Engineer (PHP MVC / REST APIs)

BD 227.273

BD 56.818 / Wk • BD 1.420 / Hr

100% Dedicated

Front-End Lead Engineer (React / UI Design Tokens)

BD 227.273

BD 56.818 / Wk • BD 1.420 / Hr

100% Dedicated

Database & Cloud DevOps Specialist

BD 204.545

BD 51.136 / Wk • BD 1.278 / Hr

100% Dedicated

QA Automation & Multi-Branch Test Lead

BD 159.091

BD 39.773 / Wk • BD 0.994 / Hr

100% Dedicated

 **Total Project Investment & Milestone Schedule in Bahraini Dinars (BHD)**

Consolidated commercial breakdown and 4-milestone payment tranche distribution for Popular Auto Spare Co.

GRAND TOTAL: BD 34,090.910

| Module Reference             | Module Domain              | Total (BHD)   | Tranche 1 (BHD) | Tranche 2 (BHD) | Tranche 3 (BHD) | Tranche 4 (BHD) | Payment Milestone Trigger                  |
|------------------------------|----------------------------|---------------|-----------------|-----------------|-----------------|-----------------|--------------------------------------------|
| MS-001                       | PCode Generation Module    | BD 3,409.091  | BD 852.273      | BD 852.273      | BD 852.273      | BD 852.273      | Demonstration & Staging Sign-Off           |
| MS-002                       | Vendor & Purchase Module   | BD 4,090.909  | BD 1,022.727    | BD 1,022.727    | BD 1,022.727    | BD 1,022.727    | Supplier Portal & 3-Way Match Verification |
| MS-003                       | Store Verification Module  | BD 5,113.636  | BD 1,278.409    | BD 1,278.409    | BD 1,278.409    | BD 1,278.409    | Scanner Verification & Cycle Count UAT     |
| MS-004                       | Sales Process & POS Module | BD 5,113.636  | BD 1,278.409    | BD 1,278.409    | BD 1,278.409    | BD 1,278.409    | Counter POS & Cash Drawer Closing UAT      |
| MS-005                       | Accounts & VAT Module      | BD 4,431.818  | BD 1,107.955    | BD 1,107.955    | BD 1,107.955    | BD 1,107.955    | GL Double-Entry & 10% VAT Return Sign-Off  |
| MS-006                       | Enterprise Admin & Fleet   | BD 4,090.909  | BD 1,022.727    | BD 1,022.727    | BD 1,022.727    | BD 1,022.727    | Asset QR Tagging & Fleet TCO Sign-Off      |
| MS-007                       | HRM & Payroll Module       | BD 5,454.548  | BD 1,363.637    | BD 1,363.637    | BD 1,363.637    | BD 1,363.637    | Biometric Sync & WPS CBB Bank Export UAT   |
| MS-008                       | Hardware & Cloud Setup     | BD 1,022.727  | BD 340.909      | BD 340.909      | BD 340.909      | —               | 3-Tier Cloud & Hardware Peripherals Setup  |
| MS-009                       | Executive BI Dashboard     | BD 1,363.636  | BD 340.909      | BD 340.909      | BD 340.909      | BD 340.909      | C-Suite Mobile Dashboard & Anomaly Alerts  |
| GRAND TOTAL INVESTMENT (BHD) |                            | BD 34,090.910 | BD 8,707.955    | BD 8,707.955    | BD 8,707.955    | BD 7,967.045    | 35 Verified Milestone Gates                |



## Governance, SLA & Payment Terms

Contractual milestones, UAT acceptance gates, and IP protection protocols

ENTERPRISE SLA

### 1. Milestone-Driven Invoicing & Payment Tranches

- **Zero Blind Upfront Risk:** Invoices are raised strictly upon completion, demonstration, and staging sign-off of each milestone tranche (25% or 33.3% per gate).
- **15-Day Verification & UAT Grace Period:** The client is entitled to a 15-calendar-day UAT review window per milestone to test all specified acceptance criteria before signing off.
- **Change Request (CR) Protocol:** Any features outside the defined scope are logged via SaNDS Lab Portal and quoted using the transparent hourly rate card (BD 8.523 / Hour).

### 2. Source Code Ownership, Security & Warranty

- **100% Intellectual Property (IP) Ownership:** Upon settlement of contract invoices, full proprietary source code, DB schemas, and deployment scripts belong exclusively to Popular Auto Spare Co.
- **Zero Third-Party Recurring Royalties:** Built on open-standard enterprise stacks (PHP 8.3 MVC, MySQL InnoDB, React 18, RabbitMQ, SQLite) with zero vendor lock-in.
- **12-Month Post-Launch Bug Warranty:** 365 days of comprehensive bug-fixing SLA and security patch support following the final production deployment of each module.

Stakeholder Authorization & Digital Sign-Off Console

By affixing digital signatures and authorizations below, all participating executive and technical stakeholders ratify the deliverables, implementation timeline, SLA commitments, and financial disbursement gates for **Master 9-Module ERP Milestone & Budget Roadmap (SL-POP-ERP-SUMMARY-001)**:

1. Engineering Preparation & Stakeholder Verification Matrix

|                                                                                                                                                                         |                                                                                                                                                                                         |                                                                                                                                                                |                                                                                                                                                                             |
|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <div>DEVELOPER / ARCHITECT</div> <div>Ancy Varghese Thekkan</div> <div>Software Architect, SaNDS Lab</div> <div>PREPARED (25-SEPTEMBER-2026)</div> <div>COMPLETED</div> | <div>VERIFIED BY (DEVELOPER)</div> <div>Ajit Kumar KV</div> <div>CEO &amp; Managing Director, SaNDS Lab</div> <div>VERIFIED (30-SEPTEMBER-2026)</div> <div>CHECKED &amp; VERIFIED</div> | <div>CONSULTANT REVIEW</div> <div>UniGlobal Business Solutions</div> <div>Project Management Consultant</div> <div>In Active Review</div> <div>IN REVIEW</div> | <div>CLIENT APPROVAL</div> <div>Popular Auto Spare &amp; A/C Parts</div> <div>Authorized Executive Signatory</div> <div>Pending Approval</div> <div>PENDING SIGNATURE</div> |
|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------|

2. Executive Multi-Party Digital Acceptance Console

|                                                                                                                                                                      |                                                                                                                                                                     |                                                                                                                                                             |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <div>Popular Auto Spare Co. W.L.L</div> <div>Client Executive Sign-off &amp; Commercial Approval</div> <div>No Signature on Record</div> <div>PENDING SIGN-OFF</div> | <div>SaNDS Lab Middle East W.L.L</div> <div>Lead Solutions Architect &amp; Engineering Director</div> <div>No Signature on Record</div> <div>PENDING SIGN-OFF</div> | <div>UniGlobal Consultancy</div> <div>Executive Strategic Advisor &amp; Governance Lead</div> <div>No Signature on Record</div> <div>PENDING SIGN-OFF</div> |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------|
